Activity ID	Activity Description	Orig Dur	Rem Dur	% Comp	Early Start	Early Finish
Grossmont Campus						
+ GRO - LIBRARY LRC (Not a Gafcon Project)						
		615	0	100	20FEB02A	29JUN04A
+ GRO - SCIENCE BUILDING						
		1,262	473	46	20FEB02A	21DEC06
+ GRO - DIGITAL ARTS / SCULPTURE						
		1,406	617	60	20FEB02A	11JUL07
+ GRO - PARKING STRUCTURE						
		922	487	31	01JUL03A	10JAN07
+ GRO - 400 BUILDING						
		1,061	627	11	02JUL03A	25JUL07
+ GRO - 200 COMPLEX (Theater Arts)						
		1,322	807	7	11MAR03A	02APR08
+ GRO - FACILITIES REPAIR PROJECTS						
		514	0	100	12MAR03A	
+ GRO - STUDENT CENTER COMPLEX						
		1,387	952	17	01JUL03A	22OCT08
+ GRO - ENERGY CONSERVATION PROJECTS						
		1,052	609	41	19JUN03A	29JUN07
+ GRO - LIFE SAFETY ROAD						
		1,293	504	40	20FEB02A	02FEB07
+ GRO - HEALTH SCIENCE BUILDING WEST 300						
		1,615	1,101	17	12MAR03A	19MAY09
+ GRO - MAINTENANCE PROJECTS						
		1,052	609	63	19JUN03A	29JUN07

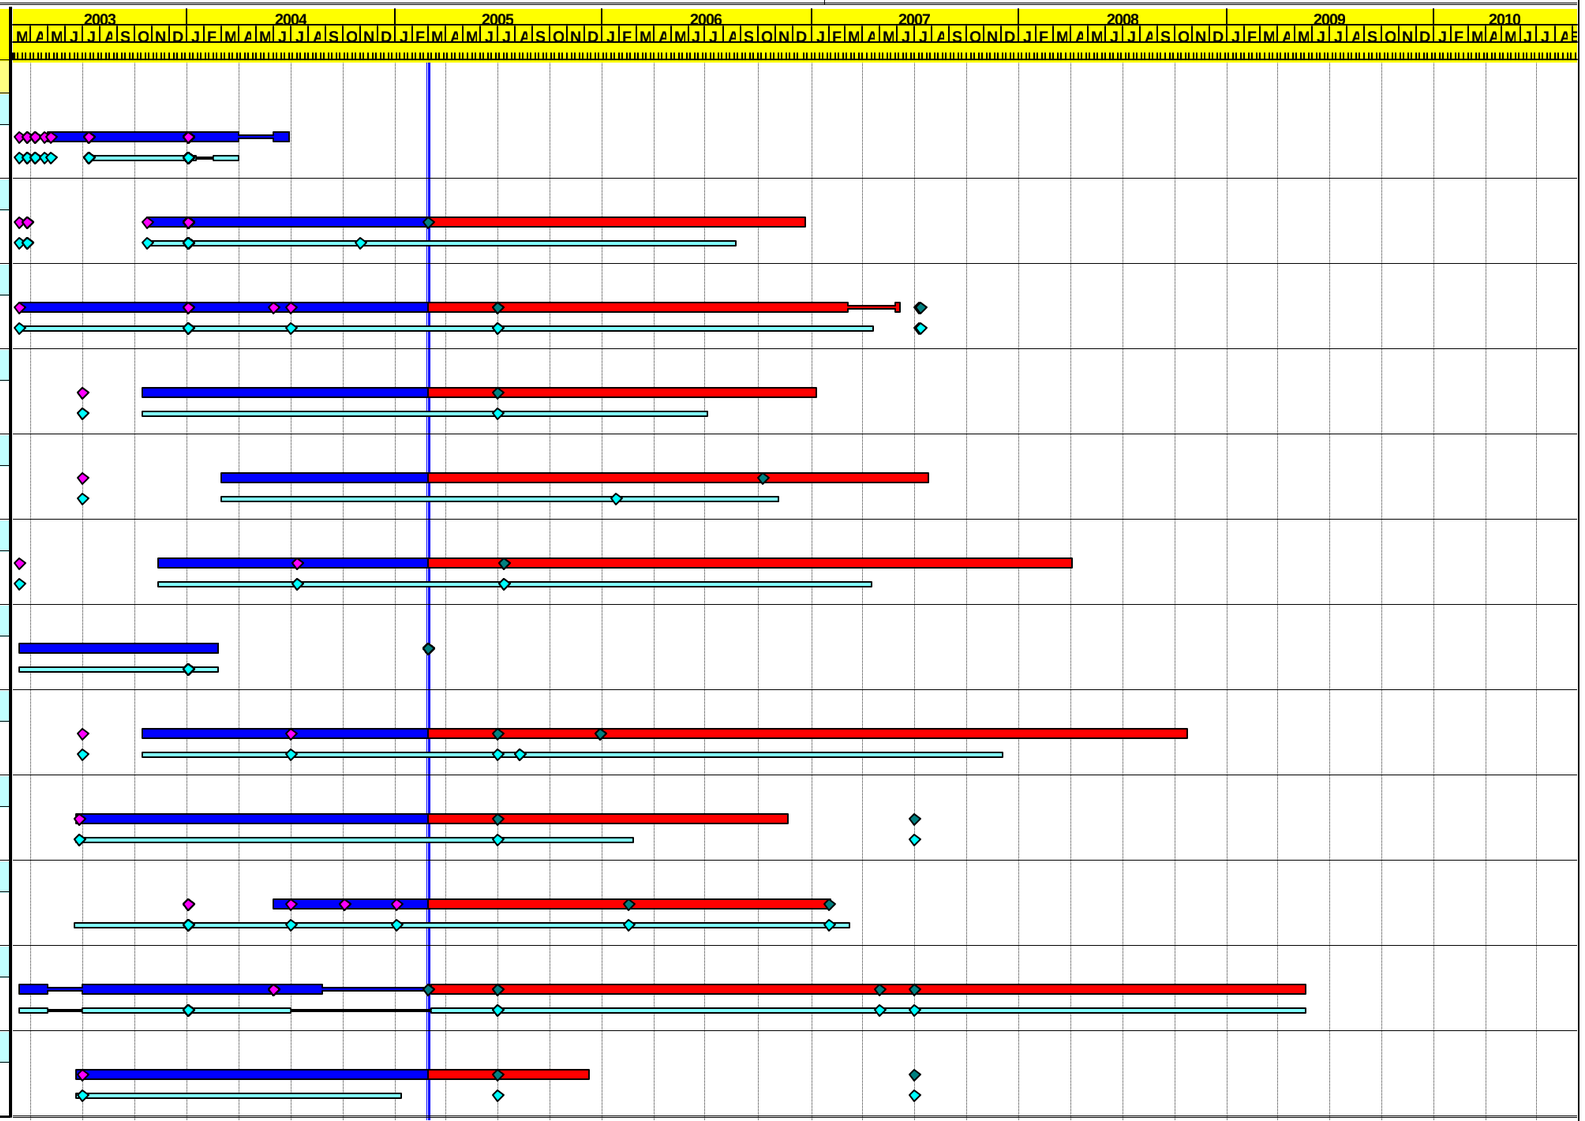

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	% Comp	Early Start	Early Finish
Cuyamaca Campus						
+ CUY - BUILDING 'O' REMODEL						
		407	40	90	03OCT03A	25APR05
+ CUY - AUTOMOTIVE TECH COMPLEX						
		564	50	94	12MAR03A	09MAY05
+ CUY - PHASE I PARKING LOT						
		526	11	96	11MAR03A	15MAR05
+ CUY - SCIENCE & TECHNOLOGY MALL						
		1,015	503	53	14MAR03A	01FEB07
+ CUY - CENTRAL PLANT, RETRO AIR HANDLERS, PIPING						
		677	162	57	11MAR03A	12OCT05
+ CUY - COMMUNICATION ARTS						
		1,045	609	57	30JUN03A	29JUN07
+ CUY - ENERGY CONSERVATION PROJECTS						
		310	0	100	28JUL03A	01OCT04A
+ CUY - STUDENT CENTER						
		964	529	37	01JUL03A	09MAR07
+ CUY - BUSINESS / CIS BUILDING						
		1,594	1,079	26	11MAR03A	17APR09
+ CUY - MAINTENANCE PROJECTS						
		373	0	100	07AUG03A	10JAN05A
+ CUY - REMODEL B,D,E,F,G						
		931	931	0	01JUL05	23JAN09
+ CUY - PARKING EXPANSION PHASE 2						
		788	788	0	02JUL07	07JUL10

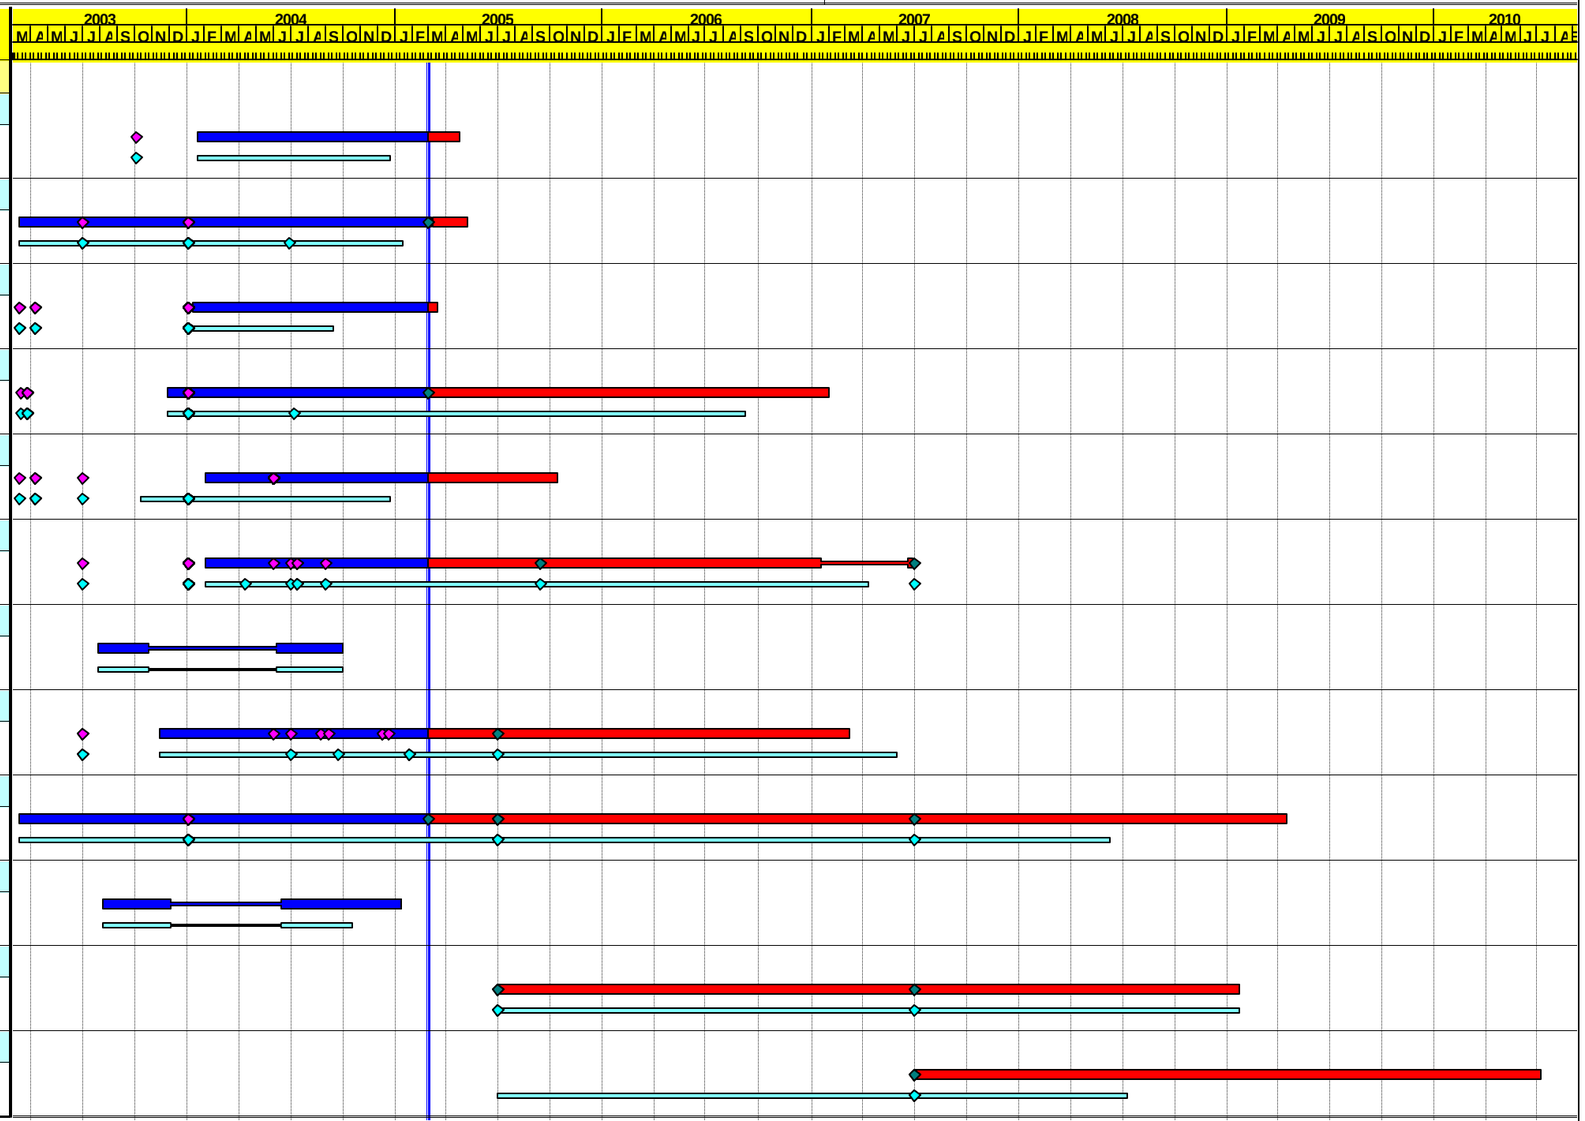

© Primavera Systems, Inc.
